| ID | Task Mode | Task Name | WBS | Duration | Start | Finish |
|---|---|---|---|---|---|---|
| 0 | | | **WP** | **804 days** | **Thu 01/09/11** | **Tue 30/09/14** |
| 1 | | **Project Management** | **WP1** | **759 days** | **Thu 01/09/11** | **Tue 29/07/14** |
| 2 | | **Project Meetings** | **WP1.1** | **683 days** | **Thu 03/11/11** | **Sun 15/06/14** |
| 3 | | Kick-off (Rome) 1st SC | WP1.1.1 | 2 days | Thu 03/11/11 | Fri 04/11/11 |
| 4 | | 1st PM (Palestine) - 2nd SC | WP1.1.2 | 2 days | Thu 01/03/12 | Fri 02/03/12 |
| 5 | | 2nd PM (Tunisia) - 3rd SC | WP1.1.3 | 2 days | Thu 27/09/12 | Fri 28/09/12 |
| 6 | | 3rd PM (Malta) - 4th SC | WP1.1.4 | 2 days | Mon 03/06/13 | Tue 04/06/13 |
| 7 | | 4th PM (Sicily) - 5th SC | WP1.1.5 | 2 days | Thu 03/10/13 | Fri 04/10/13 |
| 8 | | **Technical Meetings** | **WP1.2** | **455 days** | **Mon 11/06/12** | **Fri 07/03/14** |
| 9 | | 1st TM (Malta) | WP1.2.1 | 4 days | Mon 11/06/12 | Thu 14/06/12 |
| 10 | | 2nd TM (Palestine) | WP1.2.2 | 4 days | Sat 06/04/13 | Wed 10/04/13 |
| 11 | | 3rd TM (Tunisia) | WP1.2.3 | 4 days | Mon 01/07/13 | Thu 04/07/13 |
| 12 | | 4th TM (Rome) | WP1.2.4 | 4 days | Tue 04/03/14 | Fri 07/03/14 |
| 13 | | **Financial and Technical Report** | **WP1.3** | **661 days** | **Tue 20/03/12** | **Tue 30/09/14** |
| 14 | | 1st 6 months mon. report | WP1.3.1 | 0 days | Thu 05/07/12 | Thu 05/07/12 |
| 15 | | 2nd 6 months mon. report | WP1.3.2 | 0 days | Mon 24/12/12 | Mon 24/12/12 |
| 16 | | Interim Report | WP1.3.3 | 0 days | Wed 17/04/13 | Wed 17/04/13 |
| 17 | | 2nd Interim Report | WP1.3.4 | 0 days | Fri 31/01/14 | Fri 31/01/14 |
| 18 | | Final Financial Report | WP1.3.5 | 0 days | Tue 30/09/14 | Tue 30/09/14 |
| 19 | | **Set-up of Multistakeholders table on SWM** | **WP2** | **567 days** | **Thu 01/12/11** | **Fri 31/01/14** |
| 20 | | **Survey on Water Admin. systems in partner countries** | **WP2.1** | **132 days** | **Thu 01/12/11** | **Fri 01/06/12** |
| 21 | | Survey on water services administrations | WP2.1.1 | 55 days | Thu 01/12/11 | Wed 15/02/12 |
| 22 | | Report on water systems in MED | WP2.1.2 | 1 day | Fri 01/06/12 | Fri 01/06/12 |
| 23 | | **Creation of a database for stakeholders in partner countries** | **WP2.2** | **88 days** | **Thu 01/12/11** | **Sat 31/03/12** |
| 24 | | Identification of stakeholders for water tables | WP2.2.1 | 64 days | Thu 01/12/11 | Tue 28/02/12 |
| 25 | | Submission of the stakeholders lists to the SC | WP2.2.2 | 0 days | Wed 29/02/12 | Wed 29/02/12 |
| 26 | | **Set-up of Multistakeholders water table on natonal/regional scale** | **WP2.3** | **505 days** | **Mon 27/02/12** | **Fri 31/01/14** |
| 27 | | Organization of the 1st Water table | WP2.3.1 | 141 days | Mon 17/09/12 | Sun 31/03/13 |
| 28 | | 2nd Water table | WP2.3.2 | 109 days | Wed 01/05/13 | Mon 30/09/13 |
| 29 | | 3rd Water table | WP2.3.3 | 66 days | Mon 30/09/13 | Tue 31/12/13 |
| 30 | | Report on the Water tables concertation process | WP2.3.4 | 0 days | Fri 31/01/14 | Fri 31/01/14 |
| 31 | | **Survey on Water/Wastewater management, Households water consumption and uses** | **WP3** | **306 days** | **Thu 01/12/11** | **Thu 31/01/13** |
| 32 | | Preparation of guidelines for the data collection | WP3.1 | 43 days | Sun 01/01/12 | Tue 28/02/12 |
| 33 | | Submission of guidelines to the SC | WP3.2 | 0 days | Wed 29/02/12 | Wed 29/02/12 |
| 34 | | Data collection | WP3.3 | 109 days | Fri 01/06/12 | Wed 31/10/12 |
| 35 | | On-site investigation to survey the data collected and elaborated | WP3.4 | 22 days | Mon 10/09/12 | Tue 09/10/12 |
| 36 | | Report on water and wastewater management and household uses in MED | WP3.5 | 0 days | Mon 31/12/12 | Mon 31/12/12 |
| 37 | | **Creation of ad-hoc SWMED solutions for different target areas in MED countries** | **WP4** | **284 days** | **Mon 01/10/12** | **Thu 31/10/13** |
| 38 | | **Identification of settlements typologies in MED countries to develop the SWMED solutions** | **WP4.1** | **195 days** | **Fri 01/02/13** | **Thu 31/10/13** |
| 39 | | Socio-economic surveys on MED settlements in urban and rural areas | WP4.1.1 | 125 days | Mon 01/04/13 | Fri 20/09/13 |
| 40 | | Report on settlements adaptation to SWMED solutions | WP4.1.2 | 0 days | Mon 30/09/13 | Mon 30/09/13 |
| 41 | | **Development of tailor-made solutions for each settlement typology** | **WP4.2** | **284 days** | **Mon 01/10/12** | **Thu 31/10/13** |
| 42 | | Feasibility study on SWMED solutions for target areas | WP4.2.1 | 131 days | Mon 01/04/13 | Mon 30/09/13 |
| 43 | | Final report on tailor-made solutions for the project target areas identified | WP4.2.2 | 0 days | Thu 31/10/13 | Thu 31/10/13 |
| 44 | | **Elaboration of policy papers to use the proposed solutions in National/regional programs** | **WP5** | **522 days** | **Thu 01/03/12** | **Fri 28/02/14** |
| 45 | | Socio-economic survey on water policy effects in MED | WP5.1 | 175 days | Thu 01/03/12 | Wed 31/10/12 |
| 46 | | First draft of the policy paper on SWM in partner countries | WP5.2 | 0 days | Mon 30/09/13 | Mon 30/09/13 |
| 47 | | Presentation of the final policy paper on SWM in water and territorial planning | WP5.3 | 0 days | Fri 28/02/14 | Fri 28/02/14 |
| 48 | | **Dissmeination of best practice to benefciaries and definition of promotional policies** | **WP6** | **718 days** | **Thu 01/12/11** | **Sun 31/08/14** |
| 49 | | **Development and management of the project website** | **WP6.1** | **586 days** | **Fri 01/06/12** | **Sun 31/08/14** |
| 50 | | Activation of the project website | WP6.1.1 | 87 days | Fri 01/06/12 | Sun 30/09/12 |
| 51 | | Upload of the multistakeholder database | WP6.1.2 | 21 days | Fri 01/02/13 | Fri 01/03/13 |
| 52 | | **Upload in the intranet of financial documents from each partner** | **WP6.1.3** | **381 days** | **Fri 01/02/13** | **Fri 18/07/14** |
| 53 | | First Upload | WP6.1.3.1 | 14 days | Fri 01/02/13 | Wed 20/02/13 |
| 54 | | Second Upload | WP6.1.3.2 | 14 days | Thu 01/08/13 | Tue 20/08/13 |
| 55 | | Third Upload | WP6.1.3.3 | 14 days | Mon 02/12/13 | Thu 19/12/13 |
| 56 | | Fourth Upload | WP6.1.3.4 | 14 days | Mon 03/03/14 | Thu 20/03/14 |
| 57 | | Fifth Upload | WP6.1.3.5 | 14 days | Tue 01/07/14 | Fri 18/07/14 |
| 58 | | Upload of main project deliverables in English and Arab (synthesis) | WP6.1.4 | 325 days | Mon 03/06/13 | Fri 29/08/14 |
| 59 | | Creation of a Forum on SWM with stakeholders | WP6.1.5 | 326 days | Mon 03/06/13 | Sun 31/08/14 |
| 60 | | **Participation to conferences and paper publishing** | **WP6.2** | **173 days** | **Mon 02/09/13** | **Wed 30/04/14** |
| 61 | | Participation to water conferences | WP6.2.1 | 173 days | Mon 02/09/13 | Wed 30/04/14 |
| 62 | | Publication of articles on scientific reviews | WP6.2.2 | 86 days | Wed 01/01/14 | Wed 30/04/14 |
| 63 | | **National Information campaign** | **WP6.3** | **346 days** | **Sat 01/12/12** | **Mon 31/03/14** |
| 64 | | **Local Workshops in Italy, Malta, Tunisia and Palestine** | **WP6.3.1** | **302 days** | **Fri 01/02/13** | **Mon 31/03/14** |
| 65 | | (1) Italy and Malta, (2) Tunisia and Palestine | WP6.3.1.1 | 106 days | Fri 01/02/13 | Fri 28/06/13 |
| 66 | | (2) Tunisia and Palestine | WP6.3.1.2 | 66 days | Mon 01/07/13 | Mon 30/09/13 |
| 67 | | (2) Tunisia and Palestine | WP6.3.1.3 | 66 days | Tue 01/10/13 | Tue 31/12/13 |
| 68 | | (1) Italy and Malta, (2) Tunisia and Palestine | WP6.3.1.4 | 64 days | Wed 01/01/14 | Mon 31/03/14 |
| 69 | | Purchase of Water Saving Kits in Malta | WP6.3.2 | 45 days | Sat 01/12/12 | Thu 31/01/13 |
| 70 | | Distribution of kits in Malta | WP6.3.3 | 27 days | Thu 21/02/13 | Fri 29/03/13 |
| 71 | | Before and after monitoring master meters | WP6.3.4 | 44 days | Mon 01/04/13 | Thu 30/05/13 |
| 72 | | Purchase of Water Saving Kits in MED | WP6.3.5 | 20 days | Thu 11/04/13 | Wed 08/05/13 |
| 73 | | National Workshops in all partner countries | WP6.3.6 | 85 days | Mon 02/12/13 | Fri 28/03/14 |
| 74 | | **Equipment of laboratories in TDCs present in MED** | **WP6.4** | **304 days** | **Sat 01/09/12** | **Thu 31/10/13** |
| 75 | | Purchase of vehicle in Palestine | WP6.4.1 | 23 days | Sat 01/09/12 | Tue 02/10/12 |
| 76 | | Purchase of PC Hardware and Software in MED | WP6.4.2 | 23 days | Fri 01/02/13 | Tue 05/03/13 |
| 77 | | Purchase of small dem. water treatment systems in Palestine | WP6.4.3 | 41 days | Thu 11/04/13 | Thu 06/06/13 |
| 78 | | Purchase of demonstrative item for SWM in Tunisia | WP6.4.4 | 41 days | Thu 11/04/13 | Thu 06/06/13 |
| 79 | | Purchase of prefabricated building in Palestine | WP6.4.5 | 44 days | Mon 02/09/13 | Thu 31/10/13 |
| 80 | | Purchase of prefabricated building in Tunisia | WP6.4.6 | 44 days | Mon 02/09/13 | Thu 31/10/13 |
| 81 | | **Final Conference in TUNISIA - 6th SC** | **WP6.5** | **3 days** | **Thu 12/06/14** | **Sun 15/06/14** |

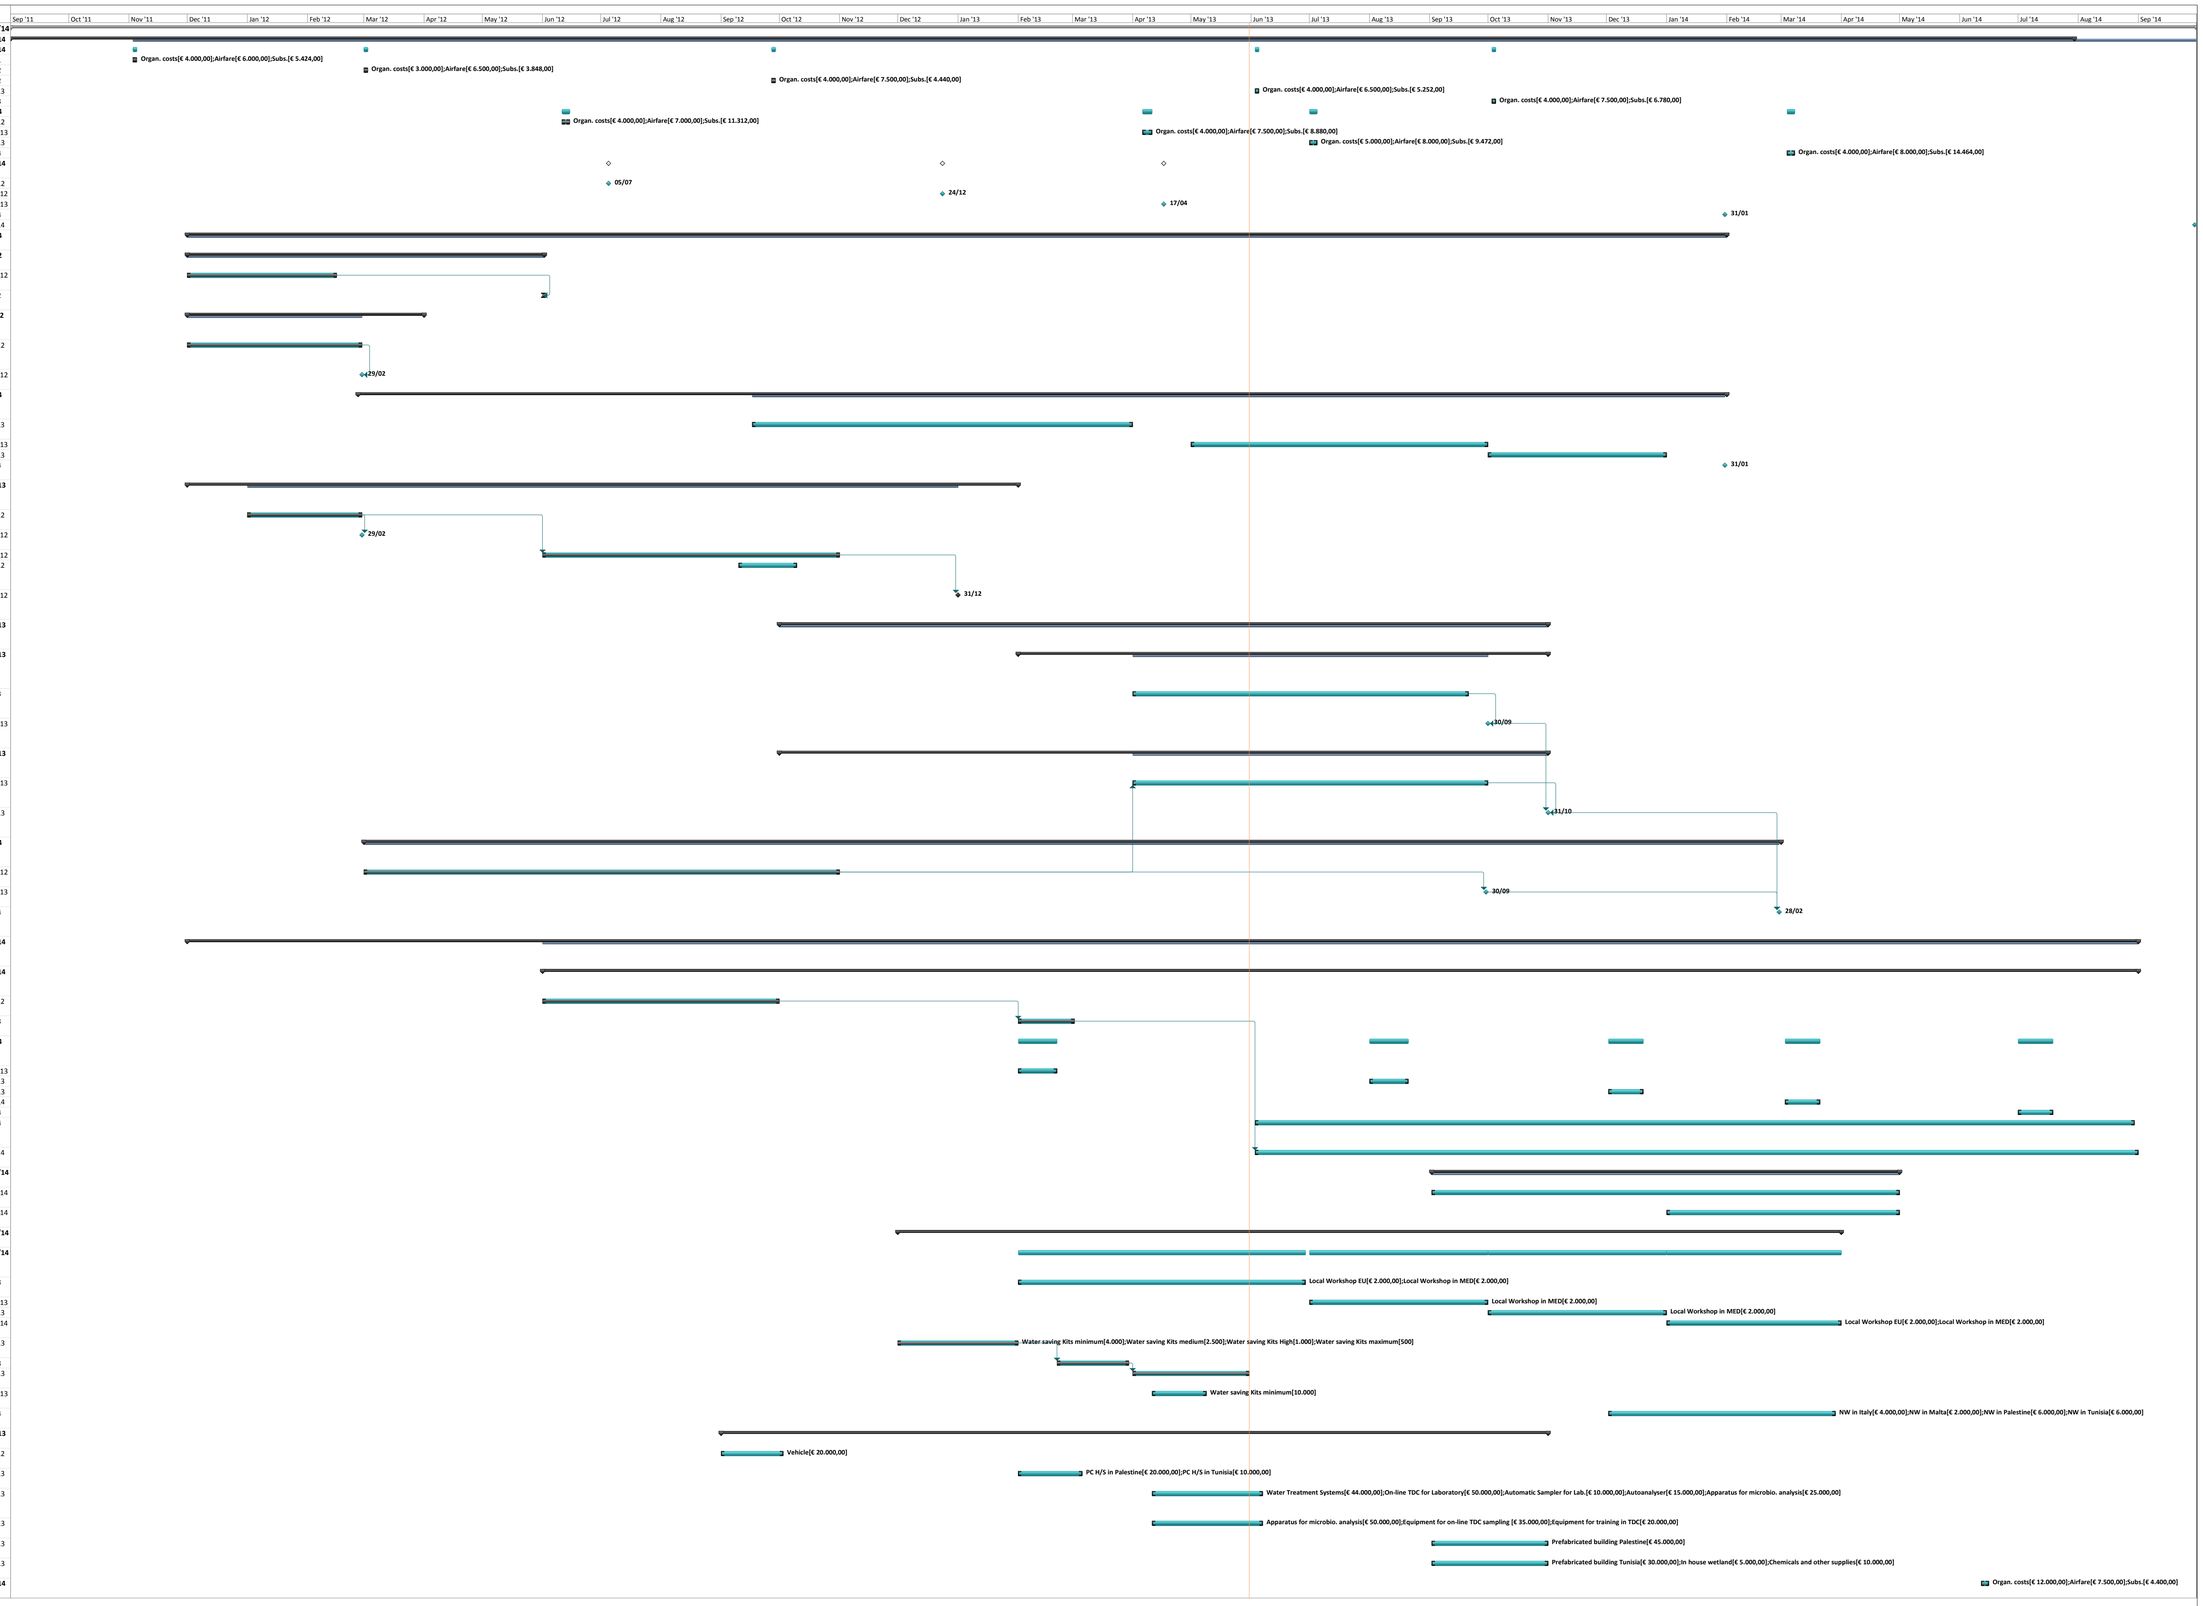


Project: SWMED - Final Gantt
Date: Fri 31/05/13

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress
